

WEEK **01**
April 12, 2019

Project Update by:
Mick Magalski / Project Manager
Office 920-751-4200 / Mobile 920-427-3133
pmagalski@mcmgrp.com

Project Update

Village of Denmark
North Wall Street (CTH T)
Hansen Street & Pine Street

NOTE TO INTERESTED PARTIES:


Additional Project information at www.mcmgrp.com under Resources\In Construction\North Wall Street (CTH T) project or you can click on the bulldozer icon on the right side of the page and select the Denmark North Wall Street project. You can also get project Tweets by following <https://twitter.com/McMNorthWallSt>

Week of Apr. 8-12

De Groot, Inc. completed the 15" sanitary sewer reconnection at the intersection of N. Wall Street and Pine Street and installed a new sanitary manhole.

Looking Ahead: Schedule for Week of Apr. 15-19

Sanitary sewer work on North Wall Street will resume next week Monday with crews proceeding south from Pine Street.

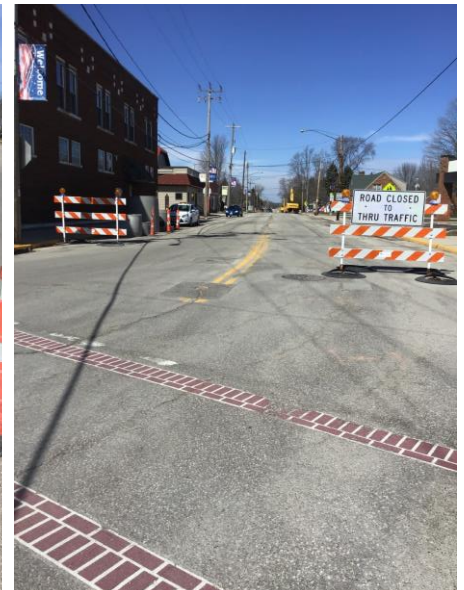

NOTES TO THE PUBLIC

The contractor will not be working onsite the remainder of this week due to weather conditions. Work operations are focused on sanitary sewer installation on North Wall Street near the Pine Street intersection. Traffic in the Pine Street intersection remains restricted with a single lane open on the north side for local traffic only. A single lane on the east side of North Wall Street remains open to local traffic currently. Through traffic should be following the marked detour route.
