


NOTE TO INTERESTED PARTIES:

Additional Project information at www.mcmgrp.com under Resources\In Construction\North Wall Street (CTH T) project or you can click on the bulldozer icon on the right side of the page and select the Denmark North Wall Street project. You can also get project Tweets by following <https://twitter.com/McMNorthWallSt>

Week of May 13-17

De Groot completed a majority of the sanitary and water service reconnections between Main St. and Highridge Ave. before switching to storm sewer construction. The contractor is working south from the culvert crossing between Pine St. and Highridge Ave.

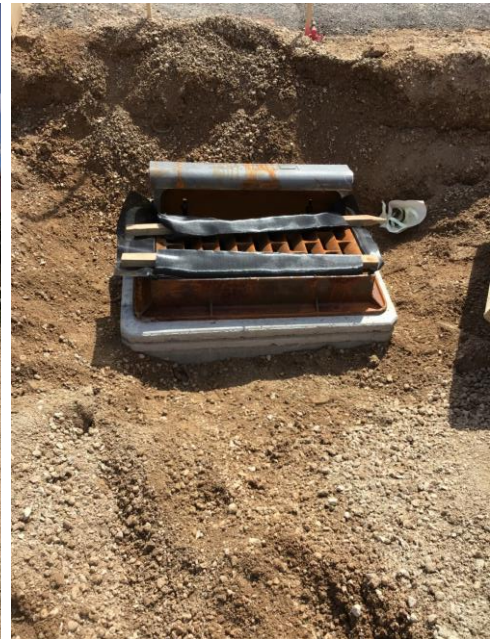

Looking Ahead: Schedule for Week of May 20-24

De Groot will continue with storm sewer construction. The contractor will also complete the new 6" water service to the Early Childhood Center and any other sanitary and water service yet to be completed between Pine St. and Highridge Ave.



NOTES TO THE PUBLIC

In the coming weeks, M&E Construction will visit the properties that are required to have the sanitary lateral replaced to the building because of the poor condition of the lateral. These residents will be receiving a letter that explains this further and times available to set up an appointment to review the laterals and obtain an estimate to complete the work.
