

NOTE TO INTERESTED PARTIES:

Additional Project information at www.mcmgrp.com under RESOURCES\In Construction...select the Belgium-2022 Storm Sewer & Street Reconstruction project. You can also get project Tweets by following <https://twitter.com/McMBelgium>


Week of October 17-21

Martell has finished up the installation of curb and gutter on the west side of the project. Soper has moved in behind them to backfill the curb and start grading on the aprons and ramps. Grading crews are continuing to work on the easements, outer pond limits and swales.




Looking Ahead to Next Week:

Restoration will continue on the west side of the project and in the easement areas. Martell will return to the site and start the installation of ramps and aprons. A grading crew will mobilize and start shaping the base in anticipation of asphalt paving.

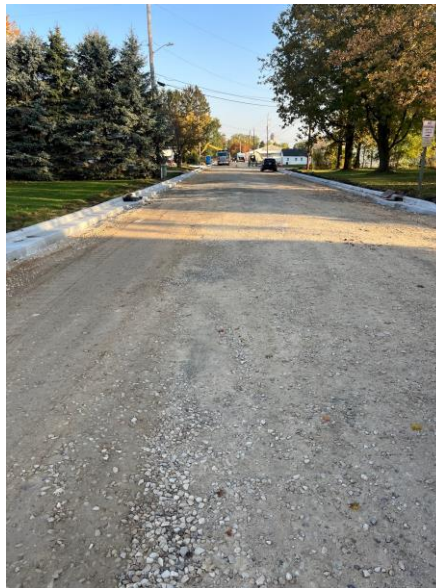

Future Schedule:

Asphalt installation will follow the installation of the curb and gutter. Crews will continue to install driveway aprons and sidewalks. Restoration of all areas will be completed once all hard surface restoration is installed.

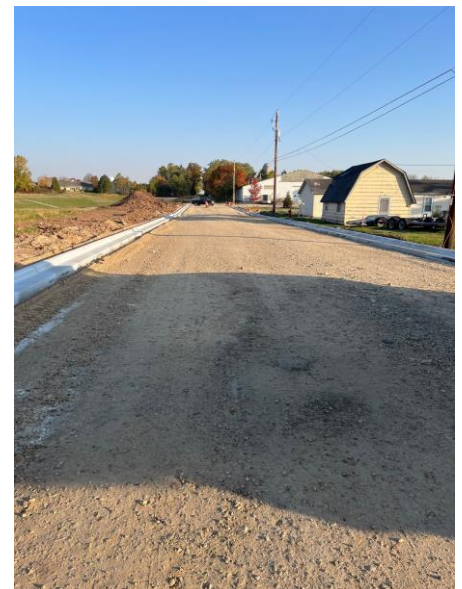

NOTES TO PUBLIC

Please travel slow and with caution on these roadways. Parking will be restricted on the roadways that are receiving concrete and asphalt paving. Contact the McMahan on-site representative or Soper with any concerns or special needs within the project area.
