

Project Update



Forest County Potawatomi Blackwell - CTH H Watermain Extension

NOTE TO INTERESTED PARTIES:

Additional Project information at www.mcmgrp.com under RESOURCES\In Construction...select the **FCPC Blackwell - CTH 'H' Watermain Extension** project. You can also get project Tweets by following <https://twitter.com/McMFCPWatermain>

Week of February 27

PTS Contractors continued with the installation of 8-inch watermain south down CTH H and have rounded the corner and are now heading west. The crew installed approximately 1500 L.F. of watermain and 3 hydrants along the west side of CTH H. The southbound lane will continue to be closed weekly Monday through Friday while the crew is working. The crew worked all week to make up lost time due to recent weather conditions. The crew plans to work 5 days next week to complete the watermain, then transition to installing the laterals.

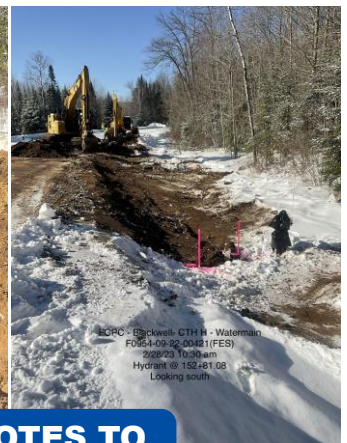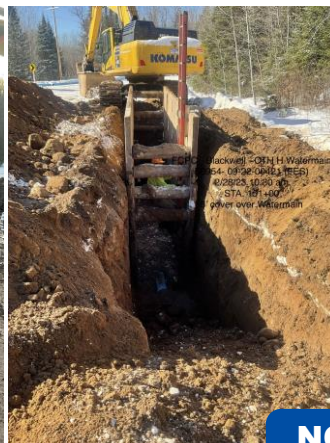

NOTES TO PUBLIC

Please be aware that the water tie-in at Kuffner Road will require a temporary shutdown of water supply to the area. The traffic control is set up and traffic patterns along CTH H are changing daily within the project limits. The lane closure may make it difficult to see oncoming traffic so please use extra caution while traveling in through the project area. Contact the McMahon on-site representative or PTS Contractors with any concerns or special needs within the project area.
