

### NOTE TO INTERESTED PARTIES:



Additional Project information at [www.mcmgrp.com](http://www.mcmgrp.com) under RESOURCES\In Construction...select the **FCPC Blackwell - CTH 'H' Watermain Extension** project. You can also get project Tweets by following <https://twitter.com/McMFCPWatermain>

### Week of March 20

Due to weight limits imposed on area roads, PTS Contractors removed equipment from the project site. Construction activities will be on-hold until weight restrictions are lifted. Erosion control devices have been placed to help with the prevention of soil loss caused by construction activities.

### Future Schedule:

Once the weight limits are removed (tentatively early May), construction can resume. In the meantime, the contractor will be making intermittent site visits to ensure the erosion control devices are being maintained.

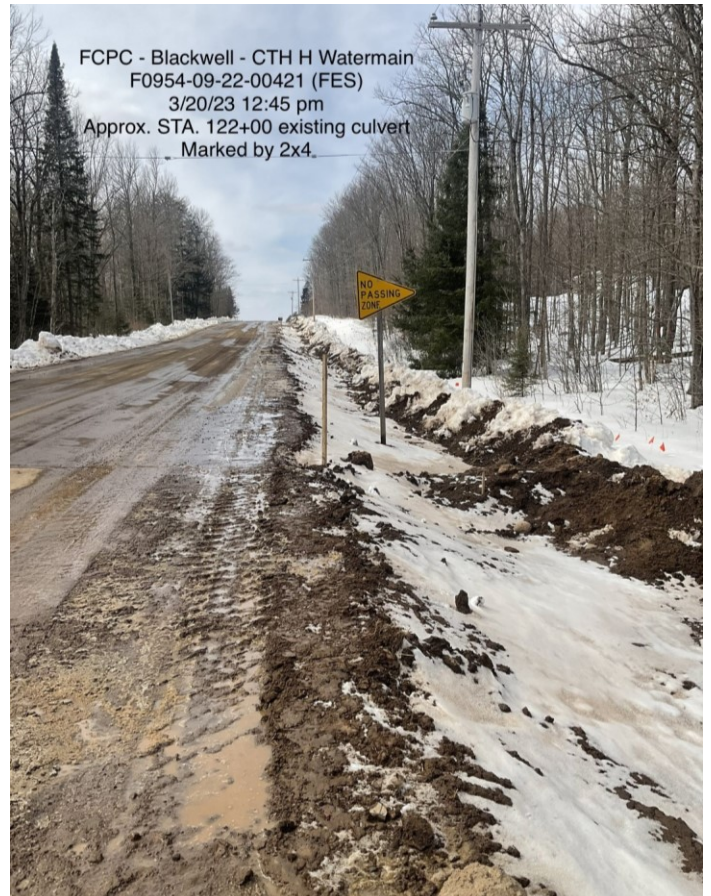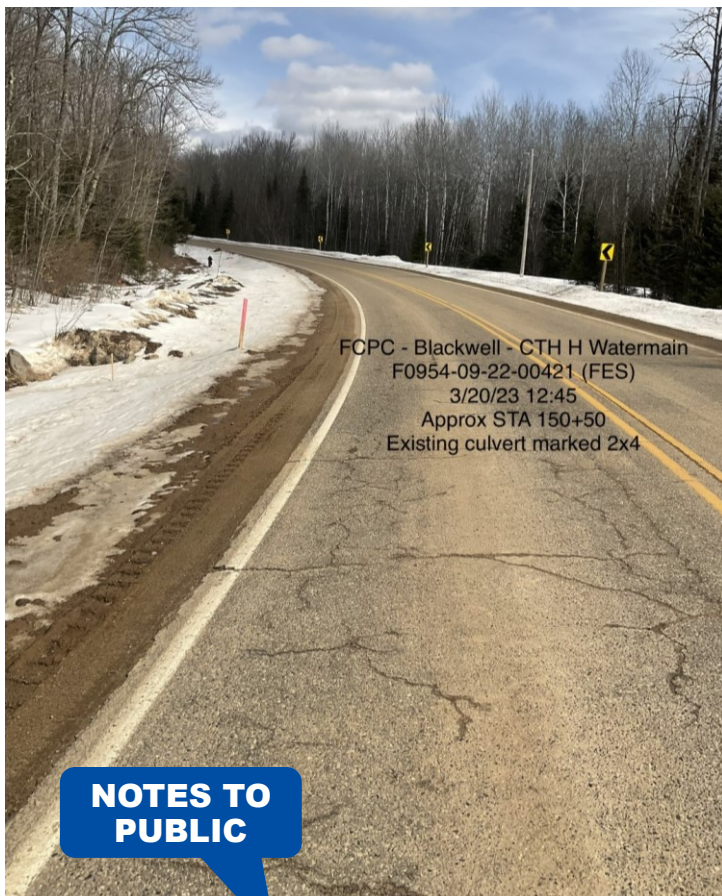

The traffic control is removed during the break in construction activities; however, the advanced warning signs will remain in place. The road will be open to traffic. There are some bumps in the road at the lateral crossings, so please use caution when crossing these areas. Contact the McMahan or PTS Contractors with any concerns or special needs within the project area.
