

### NOTE TO INTERESTED PARTIES:

Additional Project information at [www.mcmgrp.com](http://www.mcmgrp.com) under RESOURCES\In Construction...select the **FCPC Blackwell - CTH 'H' Watermain Extension** project. You can also get project Tweets by following <https://twitter.com/McMFCPWatermain>


## Week of May 22

### Gap in construction dates due to road weight restrictions

PTS Contractors has re-mobilized and started to grade the site and work on restoration by placing topsoil, seed, fertilizer with either mulch or erosion mat.

### Future Schedule:

Construction is planned to resume Tuesday, May 30th. The water main connections to the existing WM are planned for Tuesday at Kuffner Road and Wednesday at the northern end of the project. The lateral installations will take place later in the week. The transfer of services at each resident are planned for the following week along with roadway restoration.

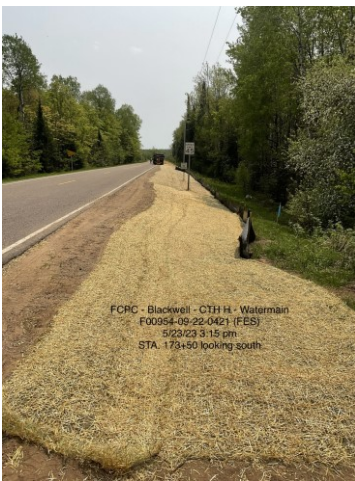

### NOTES TO PUBLIC

Roads will be open to traffic throughout the holiday weekend; however, traffic control, signage and equipment will be present in the area. With the anticipation of added holiday traffic through the weekend, please use extra caution while traveling through the site. Contact McMahon or PTS Contractors with any concerns or special needs within the project area.
