

WEEK **15**
August 15, 2025

Project Updates by:
Mike Simon, PE / Proj Mgr
Office 920-751-4200
msimon@mcmgrp.com
Jordan Jelinski / On-site
jjelinski@mcmgrp.com


Project Update

Town of Neenah - Larsen Rd (Clayton Ave - CTH CB) Road Reconstruction

NOTE TO INTERESTED PARTIES: Additional Project information at www.mcmgrp.com under RESOURCES\
In Construction...select the **Town of Neenah - Larsen Road Reconstruction** project.

Week of Aug 11-15

This week, MCC completed the placement of the road gravel West of Rocket Way as well as started to place topsoil behind the new trail on the South side of Larsen Road, starting at Oakridge Road and continuing West. Portions of the road were shut down during this phase of construction, but residents were able to get in and out of their properties. Installation of the curb did not happen this week due to unforeseen utility conflicts causing delays with the placement of road gravel.

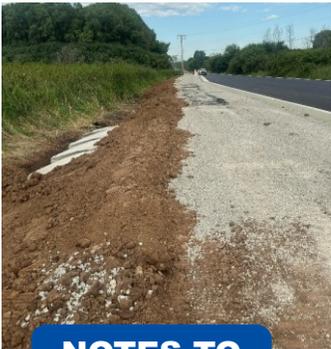

NOTES TO PUBLIC

Next Week (weather dependent):

MCC will come back to the site and continue placing topsoil on the South side of Larsen Road West of Oakridge Road. Jim Fischer Inc. will be on-site this week to place new curb on Larsen Road starting at Clayton Avenue, continuing East to roughly 300ft East of the Rocket Way intersection. The entire road will be shut down during this phase of construction, but residents will be able to get in and out of their properties. Note to the property owners on Larsen Road from the Western Project limits to 300' east of Rocket Way intersection...with the placement of the new curb and gutter, cars will need to be moved onto the road prior to curb placement, as the concrete curb and gutter needs time to cure before cars can drive over them.



Schedule

See the **revised Project Schedule** from MCC under Project Info on website. The schedule now has the project completion date as October 1st. The reason for this schedule delay is due to utility work (private utilities not owned by the Town) being completed much later than what was originally planned for the Project. With these utility relocations not being completed as originally planned, it has caused delays on the Town's Project due to conflicts with the trail and other portions of the Project as well. The Town and utilities are working together to complete the project as soon as possible.

- Larsen Road is closed to thru traffic from Clayton Avenue to CTH CB. This means that if you don't live between Clayton Avenue and CTH CB or are traveling to a destination located within these same limits, you will need to use an alternate route. Access from CTH CB to Oak Ridge Road will be maintained.
- There are no marked detour routes for this project.
- The Contractor has an up-to-date tentative schedule, posted on the project webpage under "Project Information". The contractor will be updating this schedule as-needed throughout construction.

OTHER PROJECTS IN THE AREA...

- We Energies is continuing their work on Clayton Avenue, which will cause Clayton Avenue to be reduced to one lane in certain areas. Flaggers will be utilized to help traffic flow during the day. The work being done by We Energies is not part of the Larsen Road Reconstruction Project.
- The Wisconsin DOT is continuing work on STH 76 at Larsen Road constructing a new roundabout. Larsen Road will be closed east of STH 76 while that project is on-going with no access to STH 76. Anticipated completion for roundabout is September 19th
