

WEEK **21**

September 26, 2025

Project Updates by:

Mike Simon, PE / Proj Mgr  
Office 920-751-4200

[msimon@mcmgrp.com](mailto:msimon@mcmgrp.com)

Jordan Jelinski / On-site

[jjelinski@mcmgrp.com](mailto:jjelinski@mcmgrp.com)

# Project Update

## Town of Neenah - Larsen Rd (Clayton Ave - CTH CB) Road Reconstruction

**NOTE TO INTERESTED PARTIES:** Additional Project information at [www.mcmgrp.com](http://www.mcmgrp.com) under RESOURCES\  
In Construction...select the **Town of Neenah - Larsen Road Reconstruction** project.

### Week of September 22-26

**This week, MCC and their subcontractors completed the following:**

- Continued placing topsoil on both the north and south sides of the roadway
- Continued to place seed, fertilizer, and mulch or emat
- Completed placing roadway signs
- Placed the Surface layer of asphalt
- Installed signal poles and wiring for new signals at the Rocket Way and Larsen Road intersection


### Next Week (weather dependent):

**MCC will perform the following tasks:**

- Complete installation of topsoil throughout project limits.
- Complete the placement of seed, fertilizer, and mulch or emat
- Complete pavement marking
- The road will continue to be closed during construction, but residents will be able to get in and out of their properties

### School

The Neenah Joint School District had previously sent an email to everyone in the district notifying them to not use Larsen Road. Students and/or parents of students will need to use CTH II for drop off and pick up until the Projects completion date. There will be police presence on the Project site to make sure that non-resident vehicles are not driving in the Project limits

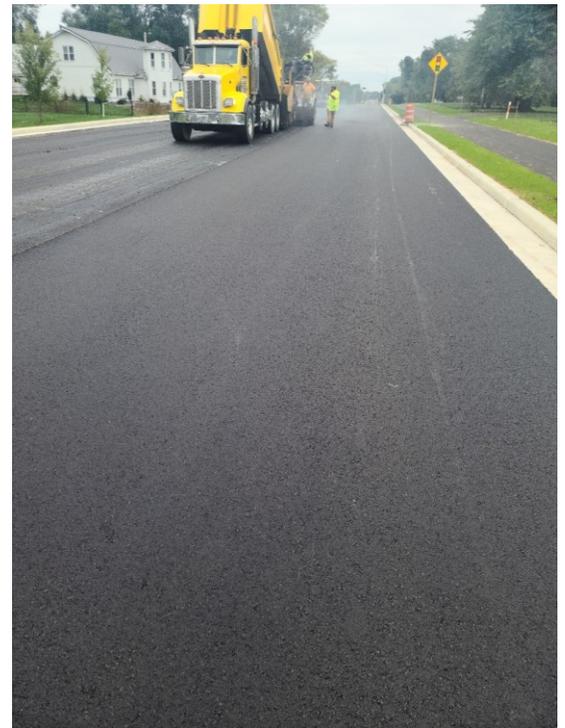

### NOTES TO PUBLIC

- Larsen Road is closed to thru traffic from Clayton Avenue to CTH CB. This means that if you don't live between Clayton Avenue and CTH CB or are traveling to a destination located within these same limits, you will need to use an alternate route. Access from CTH CB to Oak Ridge Road will be maintained.
- There are no marked detour routes for this project.
- The Contractor has an up-to-date tentative schedule, posted on the project webpage under "Project Information". The contractor will be updating this schedule as-needed throughout construction.

### OTHER PROJECTS IN THE AREA...

- The Wisconsin DOT roundabout project at STH 76 at Larsen Road was opened on Thursday of this week (9/25)
