

WEEK **04**
August 7, 2026

Project Updates by:

Mike McClone, PLS / Proj Mgr
Office 920-751-4200
mmcclone@mcmgrp.com

Fred Sommers / Onsite Rep
fsommers@mcmgrp.com

Project Update

Village of Belgium - 2026 Utility & Street Reconstruction Project

NOTE TO INTERESTED PARTIES: Additional Project information can be found at www.mcmgrp.com under **RESOURCES\In Construction** ...select the **Village of Belgium-2026 Utility & Street Reconstruction** project.

Week of August 3 - 7

The crew finished up with the mainline sanitary sewer and watermain on Antoine Drive this week. Construction of sewer and water service laterals has begun on West Lane.




Looking Ahead to Next Week:

Vinton will continue working on service laterals on West Lane and Antoine Drive. Survey staking for Storm Sewer will take place mid-week.

Future Schedule:

While work continues on installation of the sewer and water service laterals, installation of storm sewer on West Lane and Antoine Drive will begin. Pulverizing of asphalt on East Lane and Park Street will take place in the not-too-distant-future, with work then commencing on installing sanitary sewer on East Lane.

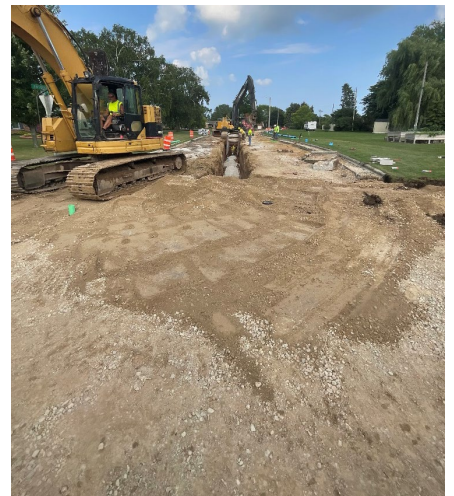

NOTES TO PUBLIC

Please drive with caution in construction areas. Contact the McMahon on-site representative or Vinton Construction with any concerns or special needs within the project area. Please be mindful of all workers in the construction zones. Thank you for your cooperation and patience.
