

WEEK **14**

October 16, 2026

Project Updates by:

Mike McClone, PLS / Proj Mgr
Office 920-751-4200

mmcclone@mcmgrp.com

Fred Sommers / Onsite Rep

fsommers@mcmgrp.com

Project Update

Village of Belgium - 2026 Utility & Street Reconstruction Project

NOTE TO INTERESTED PARTIES: Additional Project information can be found at www.mcmgrp.com under **RESOURCES\In Construction** ...select the **Village of Belgium-2026 Utility & Street Reconstruction** project.

Week of October 12 - 16

Landscaping and restoration was performed on all streets, with about 90% of that work being completed. Martell Construction poured the remainder of concrete driveway approaches and other remaining flatwork. Stark mobilized to the site, performing the fine grading of the roads on all project streets. Stark began paving the asphalt lower layer on East Lane and Antoine Drive (at the time of this writing) and hopes to get the majority of the streets paved with the first layer this week.




Looking Ahead to Next Week (weather dependent):

Vinton's asphalt paving subcontractor, Stark, will be back to pave the remaining lower layer asphalt and complete the upper layer asphalt surface on Monday and Tuesday. Miscellaneous items will be performed, like restoration along concrete driveways and resetting mailboxes, signs, etc.

If you have not done so already, please place your mailbox in a location where it can be easily accessed by the contractor.

Future Schedule (weather dependent):

The project is scheduled to be substantially completed by October 20th, with a final completion date of October 27th. Currently, the contractor is on track to meet these dates.

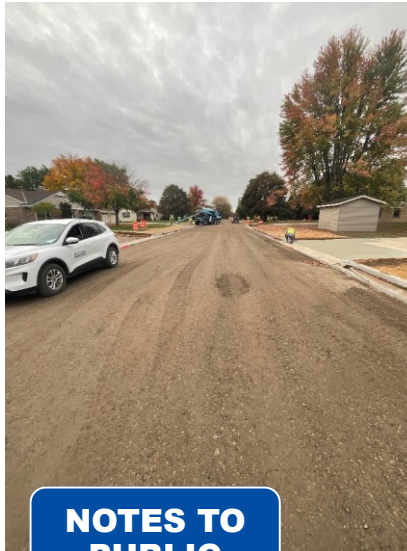

NOTES TO PUBLIC

Contact the McMahon on-site representative or Vinton Construction with any concerns or special needs within the project area. Please drive with caution and be mindful of all workers and equipment in the construction zones.
Thank you for your cooperation and patience.
