

WEEK **10**  
October 19, 2018

Project Update by:  
Matthew Greely, P.E. / Project Manager  
Office 920-751-4200 / Mobile 920-428-3604  
[mgreely@mcmgrp.com](mailto:mgreely@mcmgrp.com)

# Project Update

Town of Lawrence  
I-41 Corridor Sewer/Water


## NOTE TO INTERESTED PARTIES:

Additional Project information at [www.mcmgrp.com](http://www.mcmgrp.com) under Resources\In Construction\Lawrence I-41 Corridor Sewer Water or you can click on the bulldozer icon on the right side of the page and select the Lawrence project.

You can also get project Tweets by following <https://twitter.com/McMLawrenceI41>

## Week of Oct. 15-19

M & E Construction completed the water main borings under the culverts along Birchwood Road and Mid Valley Drive this week. They were also able to start the water main boring under I-41 at Birchwood.

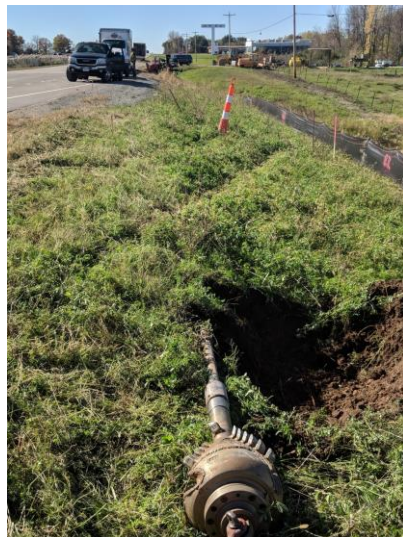

## Looking Ahead: Schedule for Week of Oct. 22-26

Carl Bowers is planning to start pavement restoration along French Road and the "Hidden Ackers" project next week. Final pavement restoration on French Road will not be completed until the final connections from the highway borings are completed.

## NOTES TO RESIDENTS

French Road is open to through-traffic. Use caution in disturbed/graveled areas. There will be limited access during paving operations along French Road.

Project information can be found on the project webpage or follow the project Twitter postings.

