

WEEK **17**
October 28, 2022

Project Updates by:

Kevin Bons/ Project Manager
Office 920-751-4200
kbons@mcmgrp.com

Mike Wright / Onsite Rep
mwright@mcmgrp.com

Project Update

Village of Belgium - 2022 Storm Sewer & Street Reconstruction

NOTE TO INTERESTED PARTIES:

Additional Project information at www.mcmgrp.com under RESOURCES\In Construction...select the Belgium-2022 Storm Sewer & Street Reconstruction project. You can also get project Tweets by following <https://twitter.com/McMBelgium>


Week of October 24 - 28

Martell has finished up the installation of curb and gutter on the west side of the project. Soper has moved in behind them to backfill the curb and start grading on the aprons and ramps. Martell has a crew on-site this week finishing up the curb gaps and forming up driveway approaches. Grading crews are continuing to work on the easements, outer pond limits and swales.




Looking Ahead to Next Week:

Restoration will continue on the west side of the project and in the easement areas. Martell will continue to install the approaches to each property. A grading crew will mobilize and start shaping the base in anticipation of asphalt paving. Asphalt paving will begin once the gravel base is prepped.

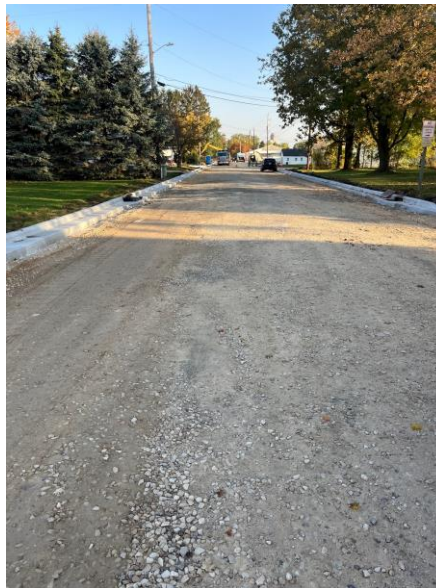

Future Schedule:

Restoration of all areas will be completed once all hard surface restoration is installed. Punch list items will be taken care of and the project will start to come to its end.

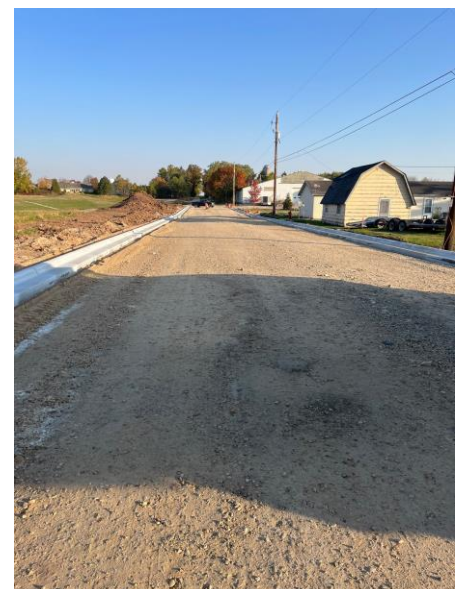

NOTES TO PUBLIC

Please travel slow and with caution on these roadways. Parking will be restricted on the roadways that are receiving concrete and asphalt paving. Contact the McMahan on-site representative or Soper with any concerns or special needs within the project area.
