

WEEK **02**
May 16, 2025

Project Updates by:
Mike Simon, PE / Proj Mgr
Office 920-751-4200
msimon@mcmgrp.com
Jordan Jelinski / On-site
jjelinski@mcmgrp.com


Project Update

Town of Neenah - Larsen Rd (Clayton Ave - CTH CB) Road Reconstruction

NOTE TO INTERESTED PARTIES: Additional Project information at www.mcmgrp.com under RESOURCES\
In Construction...select the **Town of Neenah - Larsen Road Reconstruction** project.

Week of May 12 - 16

This week, temporary erosion control devices were installed. The ditches West of Oakridge Road were temporarily re-graded to improve drainage during construction. MCC removed curb and gutter at Oakridge Road and just West of the CTH CB roundabout. On Thursday, MCC started excavating out marsh material from under the existing roadway, beginning roughly 350-ft east of the Rocket Way intersection. This material was replaced with new suitable fill material to improve the base for the new road. The full road width is being replaced during this time, which may cause some delays in local resident travel times, as they may need to travel a different route than they are used to.

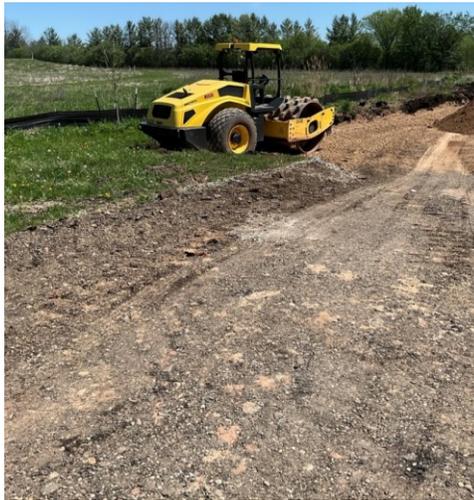

Next Week (weather dependent):

MCC will continue with removing marsh material from under the existing roadway working from Rocket Way towards CTH CB. The entire width of the road will be closed at locations where this excavation is taking place. Residents will be able to get in and out of their properties but may need to alter their normal travel route.



NOTES TO PUBLIC

- Larsen Road is closed to thru traffic from Rocket Way to CTH CB. This means that if you don't live between Rocket way and CTH CB or are traveling to a destination located within these same limits, you will need to use an alternate route. Access from CTH CB to Oak Ridge Road will be maintained.
- Larsen Road from Clayton Avenue to Rocket Way will remain open until June 9th. At that time, Larsen Road will be closed to thru traffic from Clayton Avenue to CTH CB for the duration of the project.
- There are no marked detour routes for this project.
- The Contractor presented a tentative schedule at the preconstruction meeting and property owners meeting in April. It is posted on the webpage under "Project Information". The contractor will be updating this schedule as-needed throughout construction.
