

NOTE TO INTERESTED PARTIES: Additional Project information at www.mcmgrp.com under RESOURCES\
In Construction...select the **Town of Neenah - Larsen Road Reconstruction** project.


Week of June 2 - 6

This week, MCC continued working on excavating marsh material under the existing roadway and new trail area East of the Rocket Way and Larsen Road intersection and replaced it with new suitable material to improve the base for the new road. A milestone of completing over half of the total marsh excavation for the project was reached this week. The whole road width is being replaced during this phase of construction which may cause some delays for residents. Residents may have to take a different route in comparison to what they are used to but will still have access to their property. MCC also replaced an existing driveway culvert.



Next Week (weather dependent):

MCC will continue removing marsh material under the existing roadway and new trail areas, cutting out the new North ditch line working West to East. The whole road will be shut down during this phase of construction, but residents will be able to get in and out of their property.

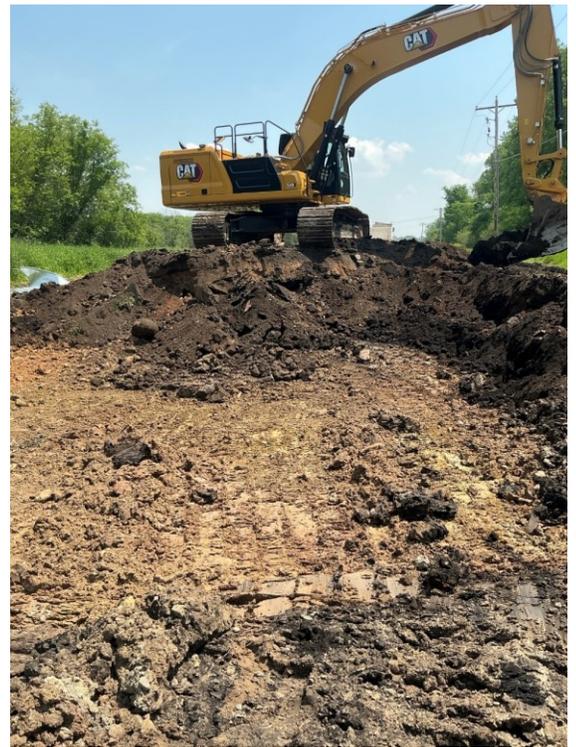

NOTES TO PUBLIC

- Larsen Road is closed to thru traffic from Rocket Way to CTH CB. This means that if you don't live between Rocket way and CTH CB or are traveling to a destination located within these same limits, you will need to use an alternate route. Access from CTH CB to Oak Ridge Road will be maintained.
- Larsen Road from Clayton Avenue to Rocket Way will remain open until June 9th. At that time, Larsen Road will be closed to thru traffic from Clayton Avenue to CTH CB for the duration of the project.
- There are no marked detour routes for this project.
- The Contractor has an up-to-date tentative schedule, posted on the project webpage under "Project Information". The contractor will be updating this schedule as-needed throughout construction.
